
Snag list

SITE	Îlot Cassiopée, 42 quai de la Fonderie, 44200 Nantes
HANDOVER	2026-09-14
INSPECTED BY	M. Ravel, Y. Sombath
REFERENCE	RS-2026-0914-03

The floor, and where each snag sits — Scale 1:300 — 48.0 m × 26.0 m

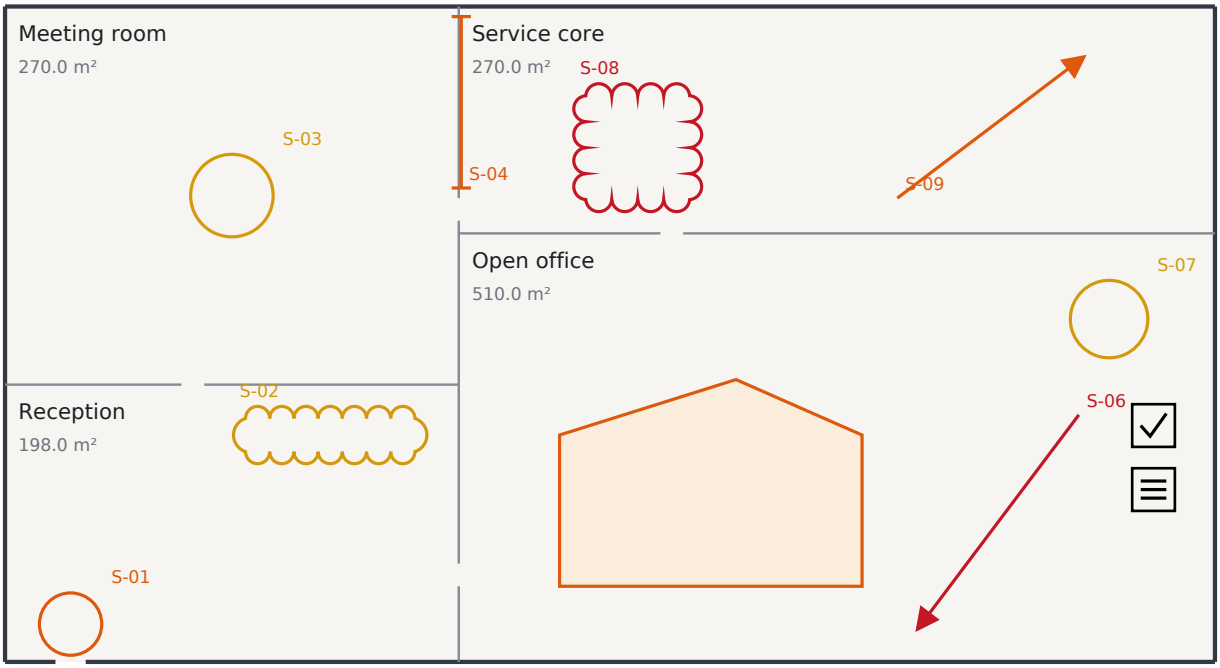

What each mark means

Cloud — the whole of the patch it runs round is under reserve.
Ring — a defect that sits at one point.
Arrow — the head rests on what the note is about.
Outline — a defect that spreads over an area of its own.
Run — a defect that follows a line, a crack, a joint or a skirting.

What each colour means

- Blocking — made good within 7 days of the handover
- Major — made good within 21 days of the handover
- Minor — made good within 30 days of the handover

Every mark on the plan says the same words as its line in the list.
Reading software shows them, hides them or leaves them off the paper.

The snags, one to a line

NO.	ROOM	WHAT WAS FOUND	DEGREE	MAKE GOOD BY	TRADE
S-01	Reception	Entrance door rubs on the floor	Major	2026-10-05	Joinery
S-02	Reception	Paint runs on the end partition	Minor	2026-10-14	Painting
S-03	Meeting room	Ceiling tile cracked over table	Minor	2026-10-14	Plastering
S-04	Meeting room	Glazed partition scratched	Major	2026-10-05	Glazing
S-05	Open office	Floor covering lifting at joints	Major	2026-10-05	Floor covering
S-06	Open office	Three sockets dead on south run	Blocking	2026-09-21	Electrics
S-07	Open office	Luminaire missing over copier	Minor	2026-10-14	Electrics
S-08	Service core	Water at the foot of the riser	Blocking	2026-09-21	Plumbing
S-09	Service core	Extract grille not connected	Major	2026-10-05	Air handling

TOTAL — 9

Every mark on the plan says the same words as its line in the list.
Reading software shows them, hides them or leaves them off the paper.

What the snags come to

Gathered by degree

DEGREE	SNAGS	SHARE
Blocking	2	22.2 %
Major	4	44.4 %
Minor	3	33.3 %
TOTAL	9	

Gathered by room

ROOM	AREA	SNAGS	SHARE
Reception	198.0 m²	2	22.2 %
Meeting room	270.0 m²	2	22.2 %
Open office	510.0 m²	3	33.3 %
Service core	270.0 m²	2	22.2 %
TOTAL	1 248.0 m²	9	

Gathered by trade

TRADE	SNAGS	SHARE
Joinery	1	11.1 %
Painting	1	11.1 %
Plastering	1	11.1 %
Glazing	1	11.1 %
Floor covering	1	11.1 %
Electrics	2	22.2 %
Plumbing	1	11.1 %
Air handling	1	11.1 %
TOTAL	9	

The last of the dates the work is to be made good by **2026-10-14**
